


Four Week Look Back:

Over the past month we have completed the following works, annotated on the image below.

2025				2026						
Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul

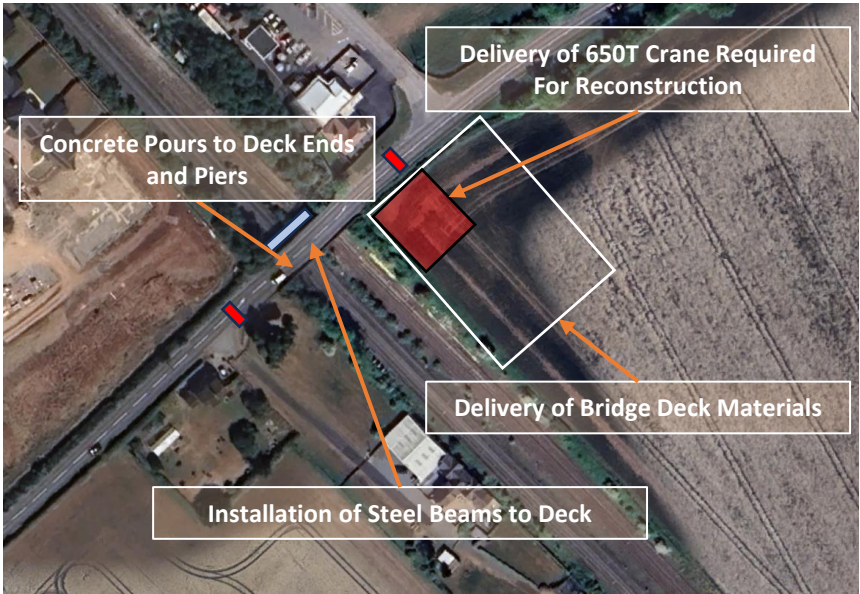

Activity	Completion Date	Status
Saw Cuts to Abutments	December 2025	Complete 
Compound Extension and Crane Pad Installation	December 2025	Complete 
Demolition of Existing Structure	December 2025	Complete 
Installation of Precast Concrete Units	December 2025	Complete 

[Web Page Link](#)
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

Programme Updates Previous Month:

The progress against the planned activities from last month are as follows:

Activity	Completion Date	Status
Remove demolition spoil and plant	January 2026	Complete 
Follow-up works (Re-profiling etc.)	January 2026	Complete 
Compound Maintenance (Post-Demolition)	January 2026	Complete 
Concrete Pours to Pier/Abutments	February 2026	Complete 
Crane Delivery for Reconstruction	February 2026	Complete 
Crane Shift – Installation of Centre Beams	February 2026	Complete 
Install Additional Access Ramp (If Required)	February 2026	Not Started

*Information is dated 18/02/2026

[Web Page Link](#)
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on
03457 11 41 41.

Programme Updates Next Month:

The planned activities over the next month are:

Activity	Completion Date	Status
Delivery of Pre-Cast Concrete Edge Beams	February 2026	In-Progress
Install Edge Beam Brackets	February 2026	In-Progress
Install Edge Beams Onto Bridge	February 2026	Not Started
Rebar and Screed Follow-On Works	February 2026	Not Started
Deliver Pre-Cast Concrete Approach Units	February 2026	Not Started
Install West Approach Units	February 2026	Not Started
Install East Approach Units	March 2026	Not Started
Demobilise Crane	March 2026	Not Started

[Web Page Link](#)
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on
03457 11 41 41.

Site Works - Look Ahead:

Our key upcoming works are:

2025				2026						
Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
	Key Activities					Completion Date		Status		
1	Traffic management installed. Site setup, including initial service diversions, service scaffold construction.					31/10/2025		Complete 		
2	Service diversions complete, site layout finalised, demolish existing bridge (piers & abutments retained).					25/12/2025		Complete 		
3	Reconstruction of bridge deck, parapet installation, deck reinforcement. Start of drainage and approach units.					22/03/2026		Planned (On-target)		
4	Installation of ducting, kerbing, road lining, tarmac surface. Completion of road safety audits. Services re-diverted.					June 2026		Planned (On-target)		
5	Completion of final road safety audit, removal of traffic management, final services re-installed.					July 2026		Planned (On-target)		




[Web Page Link](#)
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

Kirk Hill Bridge Project Monthly Newsletter (February 2026)



February 2026 Progress Photos:

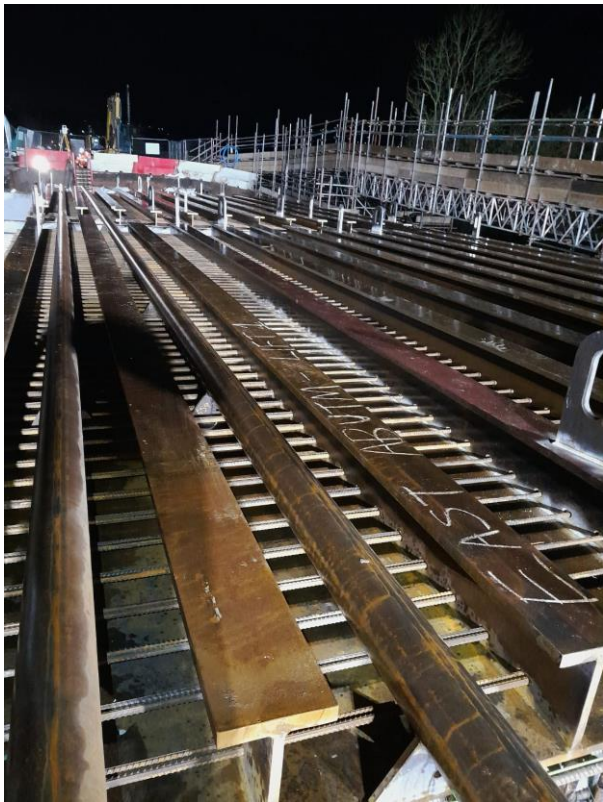

[Web Page Link](#)
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on
03457 11 41 41.

Key Communications Updates – Parish Council and Nottinghamshire County Council Meeting:

Due to increased traffic on some roads since the closure of the A6006 in September 2025, Network Rail is formalising a one-off funding contribution to Nottinghamshire County Council (NCC). This funding is intended to be used on a number of local roads being used as unofficial diversions to help address increased road safety concerns, notably pothole repairs.

NR has held a number of collaborative discussions in the last 3 weeks with Via East Midlands (Via EM), and NCC to make this happen and we are targeting the end of March 2026 latest for the funding to be with NCC. A joint statement from NR, NCC and Via EM will be issued once finalised and there will be no further updates on this matter until then.

Key Updates:

- A dedicated meeting has been held with community members and VIA to listen to concerns raised regarding road safety and the condition of local highways, with appropriate actions undertaken where applicable.
- A road sweeper is being deployed to address concerns relating to the road network in the vicinity of the compound. This service is provided a minimum of twice per week, with the capacity to increase frequency depending on site activity, deliveries, and prevailing weather conditions.
- A postcard notification has been distributed to residents and businesses in the immediate vicinity of the bridge to inform them of the planned overnight works associated with the pre-cast installation.
- Social value opportunities are currently being reviewed and will be reported in due course.

Web Page Link

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on
03457 11 41 41.

Kirk Hill Bridge Project Monthly Newsletter (February 2026)



Meetings Calendar:

Meeting dates between now and end of September are listed in the table below:

Month	Councillor Meeting	Road Safety Meeting
March	Wednesday 11 th March	Friday 13 th March Friday 27 th March
April	Wednesday 8 th April	Friday 10 th April Friday 24 th April
May	Wednesday 6 th May	Friday 8 th May Friday 22 nd May
June	Wednesday 3 rd June	Friday 5 th June Friday 19 th June
July	Wednesday 1 st July Wednesday 29 th July	Friday 3 rd July Friday 17 th July (Final before road opens)
August	Wednesday 26 th August	
September	Wednesday 23 rd September	

The last councillor session was held on 11th February, with attendance/representation from:

Nottinghamshire County Council:

Cllr Stuart Matthews
Cllr John Cottee
Cllr Bert Bingham
Cllr Andy Brown

Parish Councils:

Kegworth
Normanton on Soar
Stanford on Soar
Hathern
East Leake
West Leake
Rempstone
Sutton Bonington

Web Page Link

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.
