


Four Week Look Back:

Over the past month we have completed the following works, annotated on the image below.

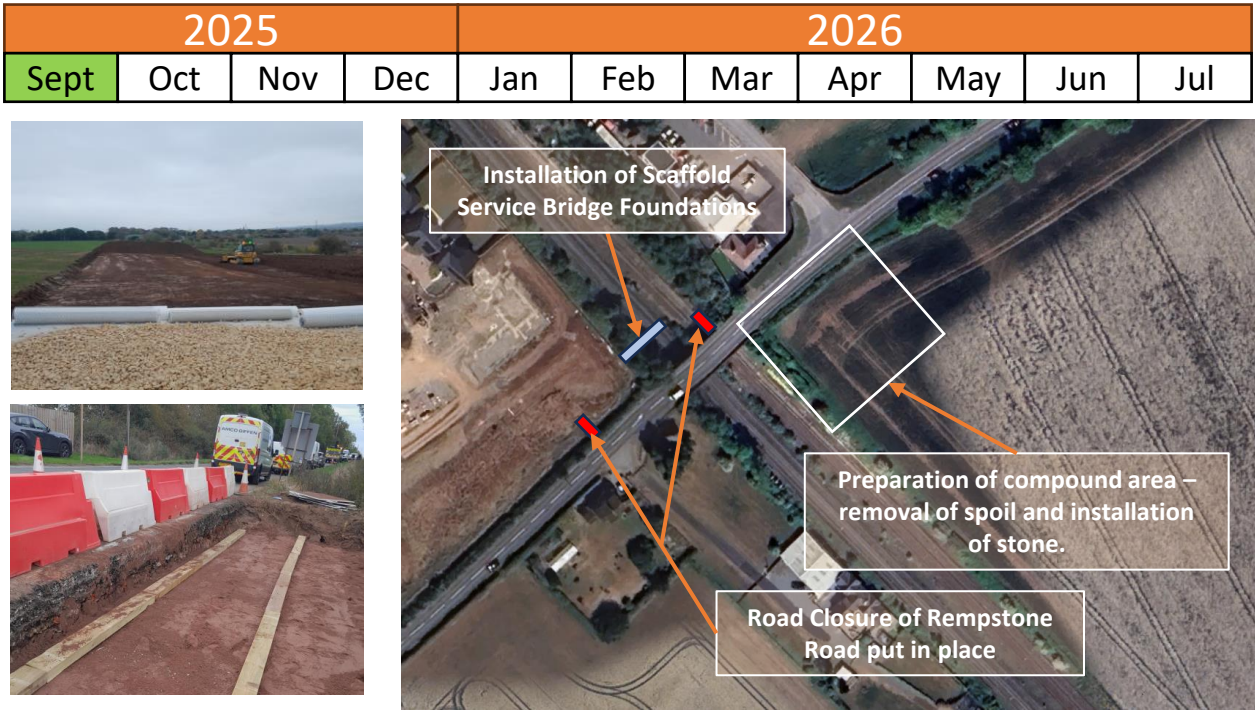

Activity	Completion Date	Status
Fencing Installation & Devegetation Works	28/09/2025	Complete 
Installation of Embankment Monitoring	28/09/2025	Complete 
Mobilisation of Compound, Installation of Access and Hedgerow Works.	03/10/2025	Complete 
Scaffold Bridge Foundations Excavated	10/10/2025	Complete 

[Web Page Link](#)
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

Programme Updates Coming Month:

The planned activities for the programme over the next month are:

Activity	Completion Date	Status
Mobilisation of BT diversions team.	06/10/2025	Complete 
Excavate roadway to expose BT services	24/10/2025	In-Progress
Completion of Temporary Service Bridge	26/10/2025	In-Progress
Installation of Main Compound	November 2025	In-Progress
Installation of cables onto temporary scaffold service bridge.	October 2025	Not Started
Mobilisation of Severn Trent	November 2025	Not Started
Mobilisation of Gas Supplier	November 2025	Not Started
Abutment Saw Cuts	November 2025	Not Started
Gas Service Excavations	November 2025	Not Started

[Web Page Link](#)
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on
03457 11 41 41.

Site Works - Look Ahead:

Our key upcoming works are:

2025				2026						
Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
	Key Activities			Completion Date			Status			
1	Traffic management installed. Site setup, including initial service diversions, service scaffold construction.			31/10/2025			In progress (On-target)			
2	Service diversions complete, demolition of existing bridge (retaining piers and abutments).			25/12/2025			Planned (On-target)			
3	Reconstruction of bridge deck, parapet installation, deck reinforcement. Start of drainage and approach units.			22/03/2026			Planned (On-target)			
4	Installation of ducting, kerbing, road lining, tarmac surface. Completion of road safety audits. Services re-diverted.			June 2026			Planned (On-target)			
5	Completion of final road safety audit, removal of traffic management, final services re-installed.			July 2026			Planned (On-target)			



[Web Page Link](#)
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

Disruptive Works – Advanced Notice:

We will be undertaking the demolition of the existing bridge deck on 25 and 26 December 2025.

We will minimise disruption during this work as much as possible. There may be some noise during the demolition of the structure. We will be using excavators to safely take apart the existing structure and remove any demolition spoil from the railway to make sure trains can run following the Christmas shutdown period.



The photos show a similar methodology, where Flying Arch bridge was demolished on 4-5 October 2025 using excavators during a 54hr period. The demolition of Kirk Hill bridge will be done in the same timeframe.



[Web Page Link](#)

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

Traffic Management:

Our traffic management arrangements are shown on the website linked at the bottom of this page.

We aim to minimise any disruption to residents while the works are taking place and would like to remind you that the businesses on Hathernware industrial estate remain open throughout the works.

Community Engagement:

We have undertaken the following community engagement over the past month:

- Public information event held at Sutton Bonington village hall on 17 September.
- Follow-up session with local businesses adjacent to the works was held on-site at the Hathernware industrial estate on 26 September.
- Regular meetings with businesses on Hathernware Industrial Estate to discuss what support can be provided over the duration of the works.
- Regular sessions with local councillors have been set up to provide updates and assurances over the works every 4 weeks.



[Web Page Link](#)

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on
03457 11 41 41.
